

Project 2A – Wheelwright WPCF Upgrades Project

Weekly Project Update (Issued on February 20, 2024)
Town of Hardwick, MA



WORK PERFORMED BY CONTRACTOR DURING THE WEEK OF FEBRUARY 12, 2024

- Installed erosion controls along perimeter of site in accordance with erosion control plan.
- Began set-up for temporary construction office and storage trailers.
- Excavated in and around existing/abandoned clarifier tanks and began demolition.
- Setup of temporary bypass pumping system in existing clearwell for proposed work on final effluent piping.
- Installed temporary electrical service to site trailers.

WORK ANTICIPATED BY CONTRACTOR DURING THE WEEK OF FEBRUARY 19, 2024

- Plans to connect electrical service to engineering and site trailers.
- Plans to continue site work, demolition and other preparatory work.

KEY WORK ELEMENTS


- Installed Erosion Controls
- Excavation and Demolition of Existing/Abandoned Clarifier Tanks
- Setup of Temporary Bypass Pumping System in Clearwell

CONTACT INFORMATION

Justin Skelly, P.E.
Senior Project Manager
413-567-6310 (x703)
justin.skelly@dpcengineering.com



Excavation and Demolition of Existing/Abandoned Clarifier Tanks

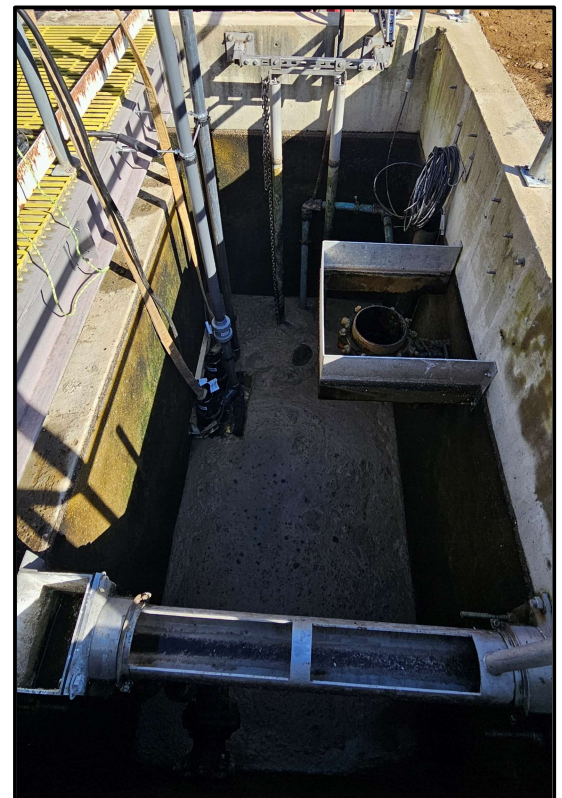

Setup of Temporary Bypass Pumping System in Existing Clearwell for Proposed Work on Final Effluent Piping
